

WILLMAR WASTEWATER TREATMENT PROJECT

March 2009 Progress Update

Wastewater Treatment Facility – Project 0812-C


Graham Construction Services has completed the following:

- Approximately 25 percent of the concrete pours for Headworks Building Structure 220. Contractor continues forming and pouring structure.



- 100 percent of excavation and installation of 54" Interceptor Piping to Headworks Building.
- Approximately 75 percent of the concrete pours for JOTS Oxidation Ditch Structure 242.
- Approximately 70 percent of the concrete pours for Municipal Oxidation Ditch Structure 244. Contractor continues forming and pouring structure.
- All underslab Processing Piping at the Secondary Building Structure 250.

- Approximately 80 percent of excavation for JOTS Clarifier Structure 252.
- Approximately 90 percent of concrete pours for Basin Drain Pump Station Structure 268.
- Approximately 25 percent of conduit for the Bio-Solids Building #1 Structure 280.

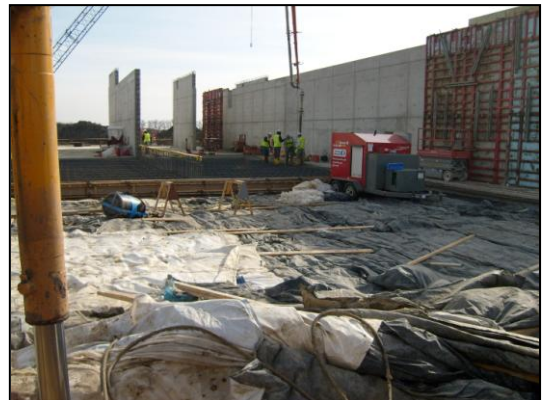

Southern Interceptor – Project 0813-D3

S.R. Weidema plans to start construction at BNSF Railroad and County Road 15 in early April 2009. Contractor continues negotiating Change Order regarding Guided Boring Method versus Microtunneling. S.R. Weidema will begin installation of Interceptor Piping at 30th Avenue SW and 15th Street SW beginning March 30, 2009. The start of this work has been delayed approximately three weeks due to weather. The intersection of 30th Avenue SW and 15th Street SW will be closed for approximately four weeks. Detour information has been provided to Willmar Township representatives and local residents.

Southern Interceptor, Forcemain and Outfall – Project 0814-D4

S.R. Weidema has installed approximately 14,000 feet of 54-inch and 48-inch Interceptor piping from the interface of Contract C toward County Road 15. Approximately 2,500 feet of Forcemain piping has been installed from the interface of Project 0812-C to East of County Road 116. County Highway 55 for been closed for approximately three weeks in order to allow open cut installation of Interceptor Piping. The Highway will be reopened within one week. PVC joint welding and infiltration testing continue.

Forcemain and Gravity Sewer – Project 0815-D5

Voss has suspended construction activities for the winter season of 2008 and will resume in April of 2009.

