

WILLMAR WASTEWATER TREATMENT PROJECT October 2008 Progress Update

Wastewater Treatment Facility – Project 0812-C

A formal Groundbreaking Ceremony was held on October 28, 2008. City of Willmar Mayor Les Heitke served as Master of Ceremonies. Representatives of the Willmar City Council, Willmar City Staff, area legislators and Donohue & Associates, Inc. were in attendance for the event.



Area legislators and City Council members throw out the first shovel of dirt at the Groundbreaking Ceremony.

Graham Construction Services continues mobilizing on site and has started mass excavation for major structures beginning with the Oxidation Ditches. They are working to establish a new access road and trailer facilities at the new plant site and is also coordinating with local utilities to provide electrical power, telephone and internet access to the site.

Southern Interceptor – Project 0813-D3

S.R. Weidema plans mobilizing on site to stage for micro-tunnel at BNSF Railroad and County Road 15. They are continuing with submittals regarding boring operations. S.R. Weidema does not plan to install any piping in City Streets until the spring of 2009.

Southern Interceptor, Forcemain and Outfall – Project 0814-D4


S.R. Weidema has installed 54" interceptor piping from the interface of Contract C to approximately County Road 116. Outfall piping is being installed behind the interceptor piping installation toward County Road 116. County Road 116 was closed on October 27 and will remain closed for approximately three weeks to allow installation of the interceptor, outfall and forcemain piping.



Forcemain and Gravity Sewer – Project 0815-D5

Voss has completed installing jack-n-bore casing under the railroad spur at Harvest States Cooperatives and is currently installing the jack-n-bore under the BNSF tracks at the Jennie-O Plant. Voss will start installing piping behind the City Ballfields north of Willmar Avenue on November 3, 2008.



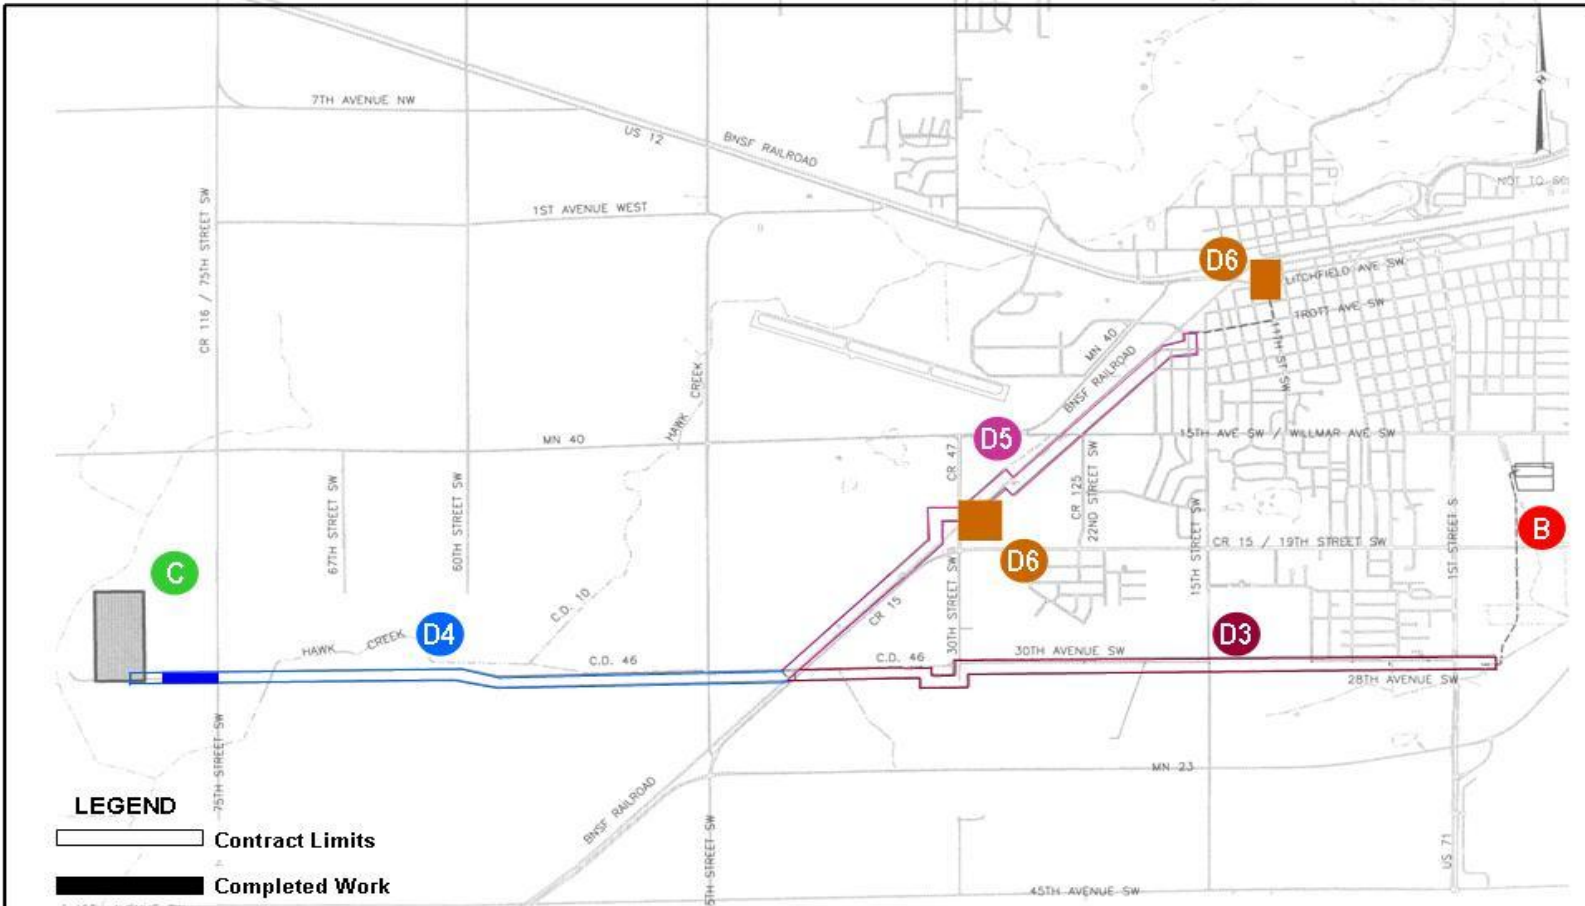

LEGEND

-  Contract Limits
-  Completed Work



**City of Willmar, Minnesota
Wastewater Program
MONTHLY PROGRESSION MAP
October 2008**

